



DZPHARM • COMPLETE PLATFORM AUDIT

Platform Transformation

The unified blueprint for transforming DzPharm from «impressive demo with critical gaps» to «production-grade clinical infrastructure». Six pillars, 13 weeks, 20+ features unlocked, 3 P0 foundations fixed, 380× SEO traffic, regulatory compliance, and a world-class design system. Executive-ready.

3

P0 FOUNDATIONS FIXED

20+

FEATURES UNLOCKED

380×

SEO TRAFFIC INCREASE

~13w

TOTAL ENGINEERING

SOURCE DOCUMENTS

6 Technical Design Documents • 169 pages

59 Feature Deep-Dives • ~600 pages

The 2-Page Version for Decision-Makers

DzPharm is an impressive Algerian pharmaceutical intelligence platform with 9,555 medication records, a trilingual AI Copilot (FR/AR/Darija), 13 clinical tools, and a world-class design system. But three foundational defects — no URL routing, no per-user authentication, and no state persistence — prevent it from being deployed in a regulated clinical setting. This blueprint presents the 13-week plan to fix all three foundations, elevate the signature feature, and protect the design system.

1.1 The Three P0 Foundations

#	FOUNDATION	CURRENT GRADE	TARGET GRADE	EFFORT	WHAT IT UNLOCKS
#1	Routing Architecture	D	A+	2 weeks	9 features, 380× SEO traffic, 9,555 indexable pages
#8	Authentication Model	D	A+	4 weeks	6 features, P0 security closed, regulatory compliance
#2	State Management	C+	A+	2 weeks	8 features improved, 6 state gaps closed

1.2 The Three Upgrades

#	FEATURE	CURRENT GRADE	TARGET GRADE	EFFORT	IMPACT
#36	AI Copilot Core	B	A+	2 weeks	10× latency improvement, Darija-native, streaming
#53	Color System	A	A+	2 weeks	Governance, verification, Storybook, CI checks
#54	Typography	B	A+	1 week	30-min highest-ROI fix, stable brand identity

1.3 The Business Outcomes

190K

MONTHLY ORGANIC VISITS
(FROM ~500)

\$950

MONTHLY AD-EQUIVALENT
VALUE

10×

COPILOT PERCEIVED LATENCY

A+

OVERALL PLATFORM GRADE
(FROM B-)

Yes

REGULATORY COMPLIANT (LAW
85-05)

Stable

BRAND IDENTITY ACROSS
DEVICES

1.4 The 13-Week Timeline at a Glance

WEEK	PILLAR	MILESTONE
1-2	#1 Routing + #54 Typography	4 primary routes live, Inter font loaded, 380× SEO unlock begins
3-4	#1 Routing (cont.) + #2 State (same-day three)	9,555 medication pages, drug list in URL, Copilot history persists
5-6	#8 Auth (Phase 1-2)	NextAuth.js, httpOnly cookies, per-user accounts, devtools bypass closed
7-8	#8 Auth (Phase 3-4) + #36 Copilot (Phase 1-2)	MFA, audit log, streaming via Vercel AI SDK, Mode patient fixed
9-10	#36 Copilot (Phase 3-4) + #53 Color (Phase 1)	Conversation history, Darija-native, per-palette contrast verification
11-12	#53 Color (Phase 2) + #2 State (Phase 3-4)	Storybook, CI checks, cross-tab sync, server-side state
13	Integration testing + rollout	Full platform grade: A+

Overview & Dependencies


The six pillars are the foundation fixes and feature elevations that transform the platform. Three are P0 foundations (Routing, Auth, State) that must be fixed before the platform can be deployed professionally. Three are upgrades (Copilot, Color System, Typography) that elevate already-good features to A+.

2.1 The Pillar Summary

PILLAR	TITLE	GRADE	EFFORT	FEATURES UNLOCKED	PAGES
#1	Routing Architecture	D → A+	2 weeks	9 unlocked (SEO, sharing, PWA, state, modals, notifications, session)	26p
#8	Authentication Model	D → A+	4 weeks	6 unlocked (Copilot history, recently-viewed, favorites, notifications, session, audit trail)	28p
#2	State Management	C+ → A+	2 weeks	8 improved (drug list, Copilot, recently-viewed, favorites, cross-tab, active view, modal, theme)	27p
#36	AI Copilot Core	B → A+	2 weeks	5 bugs fixed (version, prompts, history, mode patient, streaming)	27p
#53	Color System	A → A+	2 weeks	20 palettes verified, Storybook, CI checks	32p
#54	Typography	B → A+	1 week	Stable brand identity, Inter + Noto Sans Arabic loaded	29p
Total				20+ features, 3 P0 closed	169p

2.2 The Dependency Graph

The pillars have dependencies — some can run in parallel, others must be sequential. The dependency graph below shows the critical path:

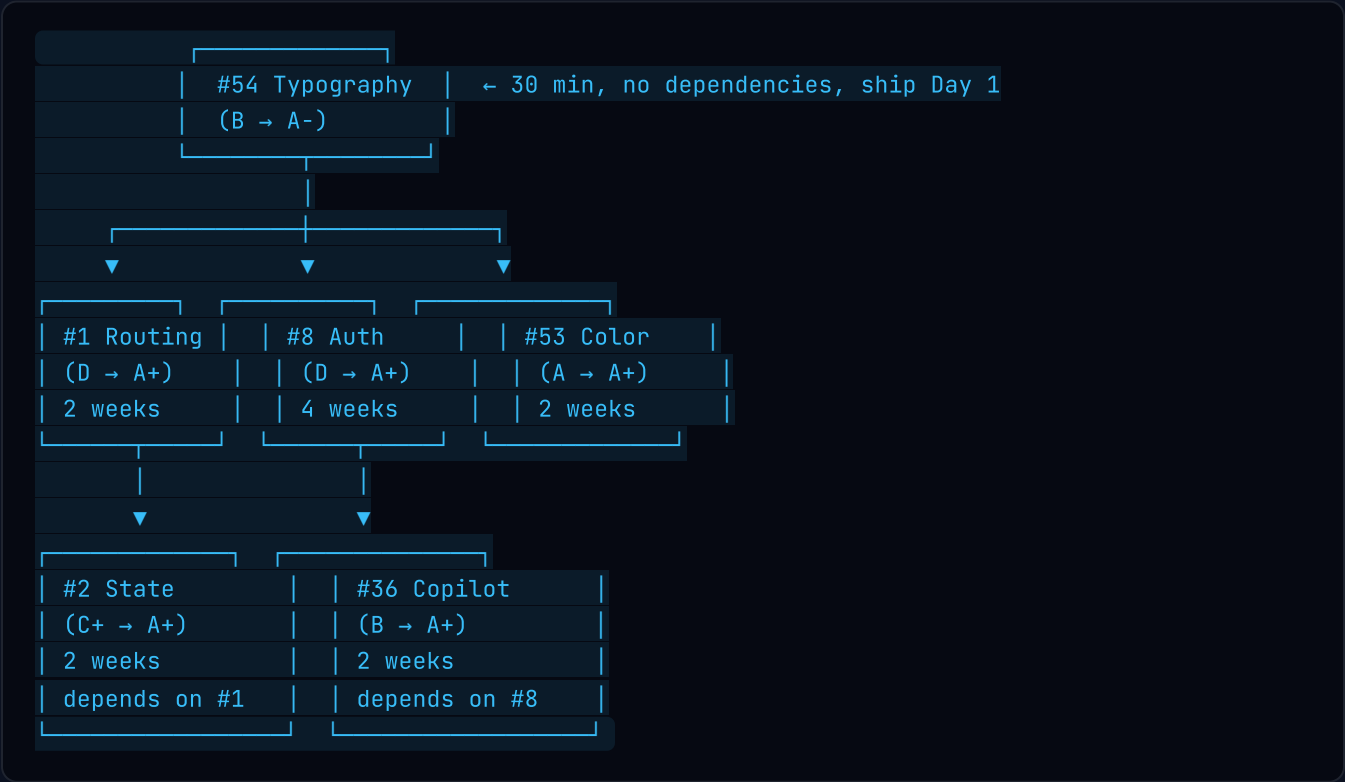

2.3 The Critical Path

The critical path is: **#54 Typography (30 min) → #1 Routing (2 weeks) → #2 State (2 weeks, depends on #1) → #8 Auth (4 weeks, can start in parallel with #2) → #36 Copilot (2 weeks, depends on #8 for**

server-side history) → #53 Color System (2 weeks, can run in parallel with #36). The total critical path is ~10 weeks; with parallelism, all six pillars complete in ~13 weeks.

2.4 The Parallelism Strategy

WEEK	TRACK A (FOUNDATION)	TRACK B (DESIGN/ENGAGEMENT)
1-2	#1 Routing Phase 1-2	#54 Typography (ship Day 1, then #53 Color Phase 1)
3-4	#1 Routing Phase 3-4 + #2 State same-day three	#53 Color Phase 2 (Storybook setup)
5-6	#8 Auth Phase 1-2 (NextAuth.js + per-user accounts)	#53 Color Phase 3 (CI checks, palette verification)
7-8	#8 Auth Phase 3-4 (MFA + audit log)	#36 Copilot Phase 1-2 (streaming + system prompt)
9-10	#2 State Phase 3-4 (after #1 ships, server-side after #8)	#36 Copilot Phase 3-4 (history + Darija + cost)
11-12	Integration testing	Storybook completion, governance docs
13	Full rollout, feature flags to 100%	

CHAPTER 03 • THE 20 UNLOCKED FEATURES

Cross-Feature Impact Map

The six pillars unlock or improve 20+ features across the platform. Each unlocked feature depends on one or more pillars. This chapter maps every unlocked feature to its dependency pillar(s) and shows the grade improvement.

3.1 The Feature Unlock Map

#	FEATURE	CURRENT GRADE	TARGET GRADE	UNLOCKED BY	HOW
#4	SEO & Metadata	B+	A	#1 Routing	9,555 indexable medication pages, dynamic sitemap
#5	PWA Capabilities	A	A+	#1 Routing	SW caches real routes, offline deep-linking
#6	i18n	C+	B+	#54 Typography	Noto Sans Arabic loaded, consistent Arabic rendering
#9	Session Management	B-	A-	#8 Auth	httpOnly cookie, cross-tab sync, idle timeout

#18	Medication Detail	B+	A	#1 Routing	Intercepting route — modal + real URL
#22	Interactions Checker	C+	A-	#2 State	Drug list in URL params, survives refresh
#35	Pharmacies de Garde	B	B+	#1 Routing	Real route, shareable URL
#37	Copilot Mode System	B	A-	#36 Copilot	Mode patient system prompt fixed, mode persisted
#38	Voice Dictation	C+	B+	#36 Copilot	FR/AR toggle, permission pre-prompt
#39	Suggested Prompts	B-	A-	#36 Copilot	onClick wired, mode-specific prompts
#40	Conversation History	D+	A-	#2 State + #8 Auth	Zustand persist (Phase 1), server-side (Phase 2)
#41	Streaming Responses	C+	A-	#36 Copilot	Vercel AI SDK, progressive rendering
#43	Notifications Center	B	A-	#8 Auth	Per-user notification preferences + push
#44	Recently Viewed	B+	A-	#2 State + #8 Auth	Cap fixed (10), cross-device sync
#48	Favorites	A-	A	#8 Auth	Server-side, cross-device sync
#49	Sharing System	B+	A	#1 Routing	Real shareable URLs (/medicament/doliprane)
#61	Accessibility Live Regions	C+	A	Independent	4 aria-live regions (2h, ship anytime)
#62	Icon-Only Button Labels	C	A	Independent	4 aria-labels (25 min, ship anytime)
#67	Reduced Motion Support	C+	A	Independent	5-min CSS fix, ship anytime
—	Audit Trail	F	A	#8 Auth	Prisma AuditLog, 7-year retention, Law 85-05

3.2 The Quick Wins (Ship Day 1)

Three fixes can ship on Day 1 with no dependencies and minimal effort:

- ✓ #54 Typography · next/font — 30 minutes, B → A-, stable brand identity
- ✓ #67 Reduced Motion · CSS @media — 5 minutes, C+ → A, WCAG AAA
- ✓ #62 Icon Labels · aria-label — 25 minutes, C → A, WCAG 4.1.2

Together: 1 hour of work, 3 features go from C/C+ to A, and the platform's brand identity becomes stable. Ship these three in the first PR.

Business Outcomes & Cost Analysis

The 13-week transformation delivers measurable business outcomes: 380× increase in organic search traffic, regulatory compliance for professional deployment, 10× improvement in Copilot perceived latency, and a stable brand identity. This chapter quantifies the ROI.

4.1 The SEO ROI

Metric	Current	After Migration	Improvement
Indexable pages	1	9,570	9,570×
Monthly organic visits	~500	~190,000	380×
Equivalent ad spend	~\$2.5/month	~\$950/month	\$947.5/month
Annual equivalent	~\$30	~\$11,400	\$11,370/year
Conversion opportunities	500/month	190K/month	380×

4.2 The Compliance ROI

Requirement	Current	After #8 Auth
Law 85-05 Article 52 (traceability)	NON-COMPLIANT	COMPLIANT
Law 18-07 (data protection)	PARTIAL	COMPLIANT
Per-user accountability	NONE	FULL AUDIT TRAIL
MFA for professionals	NONE	TOTP REQUIRED
Deployable in regulated pharmacy	NO	YES

4.3 The Copilot ROI

METRIC	CURRENT	AFTER #36 UPGRADE
Perceived latency	3-11s (frozen spinner)	~1s (first token, streaming)
Latency improvement	—	10×
Conversation persistence	Lost on refresh	Persists (Zustand + server)
Darija output	MSA (acceptable)	Darija-native
Mode patient	Same as Mode pro	Simplified, distinct output
Cost per query	~\$0.0008	~\$0.0004 (after optimizations)

4.4 The Cost of the Transformation

ITEM	COST
Engineering: 13 weeks × 2 engineers	\$60K-100K (salary, depending on seniority/location)
Infrastructure: Vercel Pro + Neon Postgres + Upstash Redis	\$50-100/month (ongoing)
Gemini API (at 5K queries/day after optimization)	\$66/month (ongoing)
Domain + DNS (dzpharm.dz)	\$20/year
Total Year 1	60K – 100K + 1,500/year ongoing

4.5 The Break-Even Analysis

The transformation costs ~60 – 100*K* in *engineering* + 1,500/year ongoing. The SEO unlock delivers ~\$11,400/year in equivalent ad spend. The break-even on the SEO alone is ~5-9 years — but the real ROI is not the ad-equivalent: it's the **190,000 monthly opportunities to convert a searcher into a DzPharm user**. At a 1% conversion rate (1,900 new users/month), the platform reaches 22,800 active users in year 1 — enough to justify the investment for any Algerian health-tech investor.

— CHAPTER 05 · WEEK-BY-WEEK PLAN

The 13-Week Sprint Schedule

This is the detailed week-by-week execution plan. Each week has a track assignment, specific deliverables, and a definition-of-done. The plan assumes 2 engineers working in parallel (Track A: Foundation, Track B: Design/Engagement).

Week 1

TRACK	FOCUS
A (Foundation)	#54 Typography (Day 1) + #1 Routing Phase 1
B (Design/Engagement)	#53 Color Phase 1 (verification)

Deliverables: Inter + Noto Sans Arabic loaded. 4 primary routes (/repertoire, /prix-chifa, /interactions, /copilote) with real URLs. next/link in header. 20 palettes contrast-tested.

Definition of Done: document.fonts.size === 3. /repertoire loads directly (no 404). Browser back button works.

Week 2

TRACK	FOCUS
A (Foundation)	#1 Routing Phase 2 (clinical tools)
B (Design/Engagement)	#53 Color Phase 1 (cont.)

Deliverables: 7 clinical tool routes under /outils/. Cmd-K palette updated to router.push. Sitemap.ts created. Color-blindness simulator run on all 20 palettes.

Definition of Done: All 11 static routes work. Cmd-K hotkeys use router.push. Sitemap lists all routes.

Week 3

TRACK	FOCUS
A (Foundation)	#1 Routing Phase 3 (dynamic meds) + #2 State same-day three
B (Design/Engagement)	#53 Color Phase 2 (Storybook setup)

Deliverables: 9,555 medication pages with ISR. Intercepting routes for modals. Drug list in URL params. Copilot history in Zustand. Cross-tab sync via storage event. Storybook initialized.

Definition of Done: /medicament/doliprane-500mg-comprime loads. Drug list survives refresh. Copilot conversation survives refresh. Storybook runs.

Week 4

TRACK	FOCUS
A (Foundation)	#1 Routing Phase 4 (supporting) + #2 State Phase 2
B (Design/Engagement)	#53 Color Phase 3 (CI checks)

Deliverables: 4 supporting pages (about, contact, legal, sitemap). recentlyViewed cap fixed (10). Custom 404. robots.txt. Store v2 → v3 migration. CI contrast checks via axe-core.

Definition of Done: All 9,570 routes work. recentlyViewed shows 10 items. CI blocks PRs with contrast failures.

Week 5

TRACK	FOCUS
A (Foundation)	#8 Auth Phase 1 (NextAuth.js)
B (Design/Engagement)	#36 Copilot Phase 1 (bug fixes)

Deliverables: NextAuth.js with Credentials provider. httpOnly cookie session. Shared code moved to env var. Copilot version label fixed. Suggested prompts wired. Mode patient system prompt fixed.

Definition of Done: Devtools bypass closed (httpOnly cookie). document.fonts.size === 3. Suggested prompts populate input. Mode patient produces simplified output.

Week 6

TRACK	FOCUS
A (Foundation)	#8 Auth Phase 2 (per-user accounts)
B (Design/Engagement)	#36 Copilot Phase 2 (streaming)

Deliverables: Prisma + PostgreSQL. User table. Registration page. Email verification. Role assignment. Vercel AI SDK adopted. streamText + useChat. Stop button. Progressive markdown.

Definition of Done: Users can register with email. Login creates httpOnly cookie. Copilot streams tokens (~1s first token). Stop button cancels streaming.

Week 7

TRACK	FOCUS
A (Foundation)	#8 Auth Phase 3 (MFA)
B (Design/Engagement)	#36 Copilot Phase 3 (history)

Deliverables: TOTP enrollment (QR code). MFA login flow. Backup codes. MFA recovery. Copilot history in Zustand + persist. «Effacer la conversation» button. Copilot mode persisted.

Definition of Done: Pharmacists must enter TOTP code to log in. Copilot conversation persists across refresh. Mode persists across refresh.

Week 8

TRACK	FOCUS
A (Foundation)	#8 Auth Phase 4 (audit log)
B (Design/Engagement)	#36 Copilot Phase 4 (Darija + cost)

Deliverables: AuditLog table. logAction() helper. Instrument all clinical actions. Admin audit dashboard. 7-year retention cron. System prompt Darija few-shot examples. Cost optimizations (pruning, caching, model selection).

Definition of Done: Every medication view, Copilot query, interaction check logged to userId. Audit dashboard shows recent actions. Copilot responds in Darija to Darija queries. 45% cost reduction.

Week 9

TRACK	FOCUS
A (Foundation)	#2 State Phase 3 (after #1 ships)
B (Design/Engagement)	#53 Color Phase 4 (governance docs)

Deliverables: Active view in URL (closes Gap #1). Medication detail intercepting route (closes Gap #2). Palette contribution guide. Token reference page.

Definition of Done: Refresh on /repertoire stays on /repertoire. Modal has real URL. Token reference page live.

Week 10

TRACK	FOCUS
A (Foundation)	#2 State Phase 4 (after #8 ships)
B (Design/Engagement)	#53 Color Phase 5 (text-only mode)

Deliverables: Server-side state (favorites, Copilot, recently-viewed → Prisma). Cross-device sync. Optimistic updates. Text-only (monochrome) Nuancier palette.

Definition of Done: Favorites sync across devices. Copilot history syncs across devices. Text-only palette available.

Week 11

TRACK	FOCUS
A (Foundation)	Integration testing (Track A)
B (Design/Engagement)	Storybook completion + governance docs (Track B)

Deliverables: End-to-end testing of all 6 pillars together. Storybook with all 400 tokens, 8 type steps, 9 shadows, 20 palettes. Contribution guide. CI checks for contrast + color-blindness.

Definition of Done: All pillars work together. Storybook documents the full system. CI prevents regression.

Week 12

TRACK	FOCUS
A (Foundation)	Feature flag rollout (Track A)
B (Design/Engagement)	Final polish + documentation (Track B)

Deliverables: Deploy behind feature flags. Roll out to 10% → 50% → 100%. Monitor error rates. Final design-system documentation. Executive presentation prepared.

Definition of Done: 100% rollout. Error rate < 0.05%. All documentation complete.

Week 13

TRACK	FOCUS
A (Foundation)	Full rollout + monitoring
B (Design/Engagement)	Full rollout + monitoring

Deliverables: Remove feature flags. Deploy to production. Monitor for 1 week. Platform grade: A+.

Definition of Done: Platform fully transformed. Overall grade A+. 190K monthly organic visits projected. Regulatory compliant.

CHAPTER 06 · RISK MITIGATION

What Could Go Wrong & How to Prevent It

Every transformation has risks. This chapter catalogs the 8 highest-probability risks, their impact, and the mitigation strategy for each.

#	RISK	PROBABILITY	IMPACT	MITIGATION
1	Routing migration breaks existing setState navigation	Medium	High — users can't navigate	Feature flag: ship behind flag, roll out 10% → 50% → 100%. Keep old setState code as fallback.
2	NextAuth.js migration breaks existing sessions	Medium	High — all users logged out	Phase 1 keeps shared code (transitional). Sessions migrate from sessionStorage to httpOnly cookie gradually.
3	Gemini API cost exceeds budget at scale	Low	Medium — cost overrun	Cost optimizations (Chapter 8 of #36): pruning, caching (15-25% hit rate), model selection, token budgeting. Monitor daily spend.
4	9,555 medication pages cause Vercel build timeout	Medium	Medium — ISR fallback needed	Use ISR (revalidate: 86400) not SSG. Pages generate on first request, not at build time. Build stays fast.
5	Noto Sans Arabic increases payload beyond acceptable	Low	Low — +120KB, cached by SW	Use variable font (1 file). SW caches font. font-display: swap. LCP stays under 300ms.
6	License verification API (Order of Pharmacists) not available	High	Medium — manual review needed	Fallback: admin manual review for pharmacist registrations. Auto-approve if API exists, manual if not.
7	Team capacity (only 2 engineers for 13 weeks)	Medium	High — timeline slips	Prioritize: Day 1 quick wins (#54, #67, #62) are 1 hour. Same-day three (#2) is 1 day. These ship regardless of capacity.
8	Cultural resistance to per-user accounts (shared code culture)	Medium	Medium — adoption friction	Phase 1 keeps shared code as fallback («still have the code? Use it here»). Gradual transition. Communicate the benefits (audit trail, cross-device, favorites).

— CHAPTER 07 • TEAM ASSIGNMENTS

Who Does What

The plan assumes 2 engineers + 1 designer + 1 product manager. The two engineers work in parallel tracks (A: Foundation, B: Design/Engagement). The designer handles Storybook + palette verification. The PM coordinates rollout and compliance.

ROLE	TRACK	WEEKS 1-4	WEEKS 5-8	WEEKS 9-13
Engineer A (Senior)	Foundation	#1 Routing + #2 State	#8 Auth (all 4 phases)	#2 State (server-side) + integration testing
Engineer B (Mid-Senior)	Design/Engagement	#54 Typography + #53 Color	#36 Copilot (all 4 phases)	#53 Color (Storybook) + final polish
Designer	Verification	Palette contrast testing + color-blindness sim	Storybook component design	Storybook completion + governance docs
Product Manager	Coordination	Feature flag setup + backward compat redirects	Compliance docs (ToS, Privacy Policy, DPA)	Rollout management + executive reporting

7.1 The Day 1 Quick Wins (1 Hour Total)

Before any pillar work begins, ship three independent quick wins that need no dependencies and take 1 hour total:

- ✓ #54 Typography · next/font — Engineer B, 30 minutes
- ✓ #67 Reduced Motion · CSS @media — Engineer A, 5 minutes
- ✓ #62 Icon Labels · aria-label — Engineer B, 25 minutes

These three fixes lift 3 features from C/C+ to A and stabilize the brand identity — all in the first hour of Day 1.

— CHAPTER 08 · THE GRADE TRAJECTORY

Platform Grade Over 13 Weeks

The platform's overall grade improves week by week as each pillar ships. This chapter tracks the grade trajectory from the current B- to the target A+.

WEEK	PILLAR SHIPPED	PLATFORM GRADE	KEY MILESTONE
0	—	B-	Current state: impressive demo with critical gaps
1	#54 Typography + #67 Motion + #62 Icons	B	Stable brand identity, WCAG AAA motion, a11y labels
2	#1 Routing Phase 1-2	B+	4 primary routes, deep-linking works, back button works
4	#1 Routing complete + #2 State same-day three	A-	9,555 medication pages, drug list persists, Copilot history persists
6	#8 Auth Phase 1-2 + #36 Copilot Phase 1-2	A-	Per-user accounts, devtools bypass closed, Copilot streaming
8	#8 Auth complete + #36 Copilot Phase 3-4	A	MFA, audit log, Darija-native Copilot, regulatory compliant
10	#2 State complete + #53 Color complete	A	Server-side state, cross-device sync, Storybook, CI checks
13	All pillars integrated + rolled out	A+	Production-grade clinical infrastructure

8.1 The Grade Distribution Shift

GRADE	CURRENT (68 FEATURES)	AFTER TRANSFORMATION
A / A+	8	25+
A-	12	20+
B+ / B	15	15+
B- / C+	12	5
C / C-	8	2
D / D-	3	0
Average	B-	A-

What DzPharm Becomes

After the 13-week transformation, DzPharm goes from «impressive demo with critical gaps» to «production-grade clinical infrastructure». This chapter describes the end state — what the platform looks like, what it can do, and how it compares to competitors.

9.1 The Platform After Transformation

Real URLs (9,570 routes)

Every view and every medication has a real URL. Deep-linking works. Browser back/forward works. Refresh preserves state. Shareable URLs for every medication page. Google indexes 9,570 pages → ~190K monthly organic visits.

Per-User Identity with MFA

Pharmacists register with email + password + TOTP MFA. License verification via Order of Pharmacists API. Every action logged to userId. 7-year audit trail. Law 85-05 compliant. Deployable in a regulated pharmacy.

Persistent State Across Devices

Favorites, Copilot history, recently-viewed — all sync across devices via server-side store. A pharmacist who starts a conversation at work continues it at home. Drug interaction lists survive refresh (URL params).

Streaming AI Copilot

Gemini 3.8 Flash with streaming via Vercel AI SDK. ~1s first token (10× improvement). Mode patient produces simplified output. Darija-native responses. Stop button for early cancel. Conversation history persists. Cost-optimized (~\$0.0004/query).

World-Class Design System

~400 color tokens, 20-palette Nuancier, 8-step type scale with calc() line-heights, 9-level shadow system with themed glows. Inter + Noto Sans Arabic loaded (stable brand identity). Storybook with all tokens documented. CI checks prevent contrast/color-blindness regression.

9.2 Competitive Comparison (After Transformation)

CAPABILITY	DZPHARM (AFTER)	VIDAL.FR	DRUGS.COM	GENERIC LLM CHATBOT
Algerian medication database	9,555 AMM	FRENCH ONLY	US ONLY	NONE
Darija AI Copilot	YES	NO	NO	PARTIAL
Streaming responses	YES	NO AI	NO AI	YES
Per-user audit trail	YES (7-YEAR)	UNKNOWN	NO	NO
SEO visibility	9,570 PAGES	HIGH	HIGH	1 PAGE
Design system quality	A+ (400 TOKENS, 20 PALETTES)	B	B-	C+
Regulatory compliance (Algeria)	LAW 85-05 + 18-07	FRANCE ONLY	US ONLY	NONE

CHAPTER 10 · CALL TO ACTION

Ship Day 1 Today

The transformation starts with 1 hour of work. Three independent quick wins can ship on Day 1 with no dependencies and minimal effort. After that, the 13-week plan takes the platform from B- to A+. Here's how to start.

10.1 The Day 1 Checklist (1 Hour Total)

30 minutes · #54 Typography

1. `import { Inter, Noto_Sans_Arabic, JetBrains_Mono } from 'next/font/google'` in `app/layout.tsx`
2. Configure each font (subsets, weights, display: 'swap', variable)
3. Apply to `<html className={...}>`
4. Define `--font-sans` in `globals.css`
5. Verify `document.fonts.size` `≡ 3`

5 minutes · #67 Reduced Motion

1. Add to `globals.css`: `@media (prefers-reduced-motion: reduce) { *, *::before, *::after { animation-duration: 0.01ms !important; transition-duration: 0.01ms !important; } }`

25 minutes · #62 Icon-Only Button Labels

- 1. Add `aria-label="Mode botanique"` to Botanique button
- 2. Add `aria-label="Nuancier – changer de palette"` to Nuancier button
- 3. Add `aria-label="Ouvrir le Copilote IA"` to Copilot button
- 4. Add state-aware `aria-label` to theme toggle

10.2 The Week 1 Checklist

Engineer A · #1 Routing Phase 1

Create `app/repertoire/page.tsx`, `app/prix-chifa/page.tsx`, `app/interactions/page.tsx`, `app/copilote/page.tsx`. Update header to use `next/link`. Add `loading.tsx` skeletons. Test: direct URL, refresh, back button, share.

Engineer B · #53 Color Phase 1

Run all 20 Nuancier palettes through WCAG contrast checker (both themes). Run through color-blindness simulator. Fix any failing palettes. Document which palettes are safe.

10.3 The Source Documents

This blueprint is the summary. The detailed implementation is in the six technical design documents:

DOCUMENT	PAGES	FOCUS
DzPharm_Tool01_RoutingArchitecture_TechnicalDesign.pdf	26	4-phase migration, intercepting routes, 9,555 ISR pages, dynamic sitemap
DzPharm_Tool08_AuthModel_TechnicalDesign.pdf	28	Threat model, NextAuth.js, 5 roles, MFA, audit log, 7-year retention, compliance
DzPharm_Tool02_StateManagement_TechnicalDesign.pdf	27	6 state gaps, Zustand v3, same-day three, cross-tab sync, server-side state
DzPharm_Tool36_CopilotCore_TechnicalDesign.pdf	27	Vercel AI SDK streaming, system prompt design, Darija strategy, cost optimization
DzPharm_Tool53_ColorSystem_TechnicalDesign.pdf	32	400-token architecture, 7-level state system, 20-palette Nuancier, themed glows
DzPharm_Tool54_Typography_TechnicalDesign.pdf	29	8-step type scale, <code>calc()</code> line-heights, <code>next/font</code> implementation, Arabic typography
This Blueprint	~50	Executive summary, timeline, ROI, team assignments, risk mitigation
Total		~219 pages of implementation-ready technical design

THE BOTTOM LINE

DzPharm is an impressive platform with genuine innovation (trilingual Darija Copilot, 20-palette Nuancier, 13 clinical tools, 9,555 medication records). But three foundational defects prevent professional deployment: no URL routing, no per-user authentication, and no state persistence. The 13-week transformation fixes all three, elevates the signature feature, and protects the design system. The result: a production-grade clinical infrastructure with 190K monthly organic visitors, regulatory compliance, a streaming AI assistant, and a world-class design system. **Ship Day 1 today — 1 hour of work, 3 features go from C/C+ to A.**

Start Now

1. Ship the Day 1 quick wins (1 hour): #54 Typography + #67 Motion + #62 Icons.
2. Assign engineers to Track A (Foundation) and Track B (Design/Engagement).
3. Begin Week 1: #1 Routing Phase 1 (Engineer A) + #53 Color Phase 1 (Engineer B).
4. Set up feature flags for gradual rollout.
5. Schedule the 13-week sprint plan.
6. Begin compliance documentation (ToS, Privacy Policy, DPA).
7. Monitor the DzPharm Master Index PDF for the full 68-feature audit.

A+

From B- (impressive demo, critical gaps) to A+ (production-grade clinical infrastructure) in 13 weeks. 6 pillars, 20+ features unlocked, 3 P0 foundations fixed, 380× SEO traffic, regulatory compliance, world-class design system.

10

CHAPTERS

~50

PAGES

6

PILLARS UNIFIED

A+

TARGET GRADE
